

Suite 214 coordination transmittal

Orion Biologics | Laboratory renovation | Issue for construction coordination

REVISION C

ISSUE SUMMARY

Revision C incorporates the answered access-control RFI, updates the Lab B corridor door identifier, assigns the card reader circuit, and carries the coordinated rack and network sheets issued on 12 June 2026.

DOCUMENT REGISTER

Sheet	Title	Revision	Issue date	Status
A2.14	Suite 214 floor plan	C	12 Jun 2026	Coordinated
T4.08	Rack R2 elevation and ports	C	12 Jun 2026	Coordinated
N1.07	Laboratory network topology	C	12 Jun 2026	Coordinated
E6.02	Panel LP-2 schedule	C	12 Jun 2026	Coordinated
RFI-214B	Lab B corridor door	Answered	12 Jun 2026	Attached scan


REVISION HISTORY

Revision	Date	Change	Issued by
A	28 May	Existing-condition backgrounds	M. Song
B	07 Jun	Lab B door shown as D-214A	M. Song
C	12 Jun	Door D-214B; CR-6; circuit L2-15	A. Verma

Revision C controls. The D-214A identifier remains only on the attached marked-up Revision B RFI sheet.

A2.14 - Suite 214 floor plan


Field dimensions, egress direction, equipment callouts, and coordinated door identity

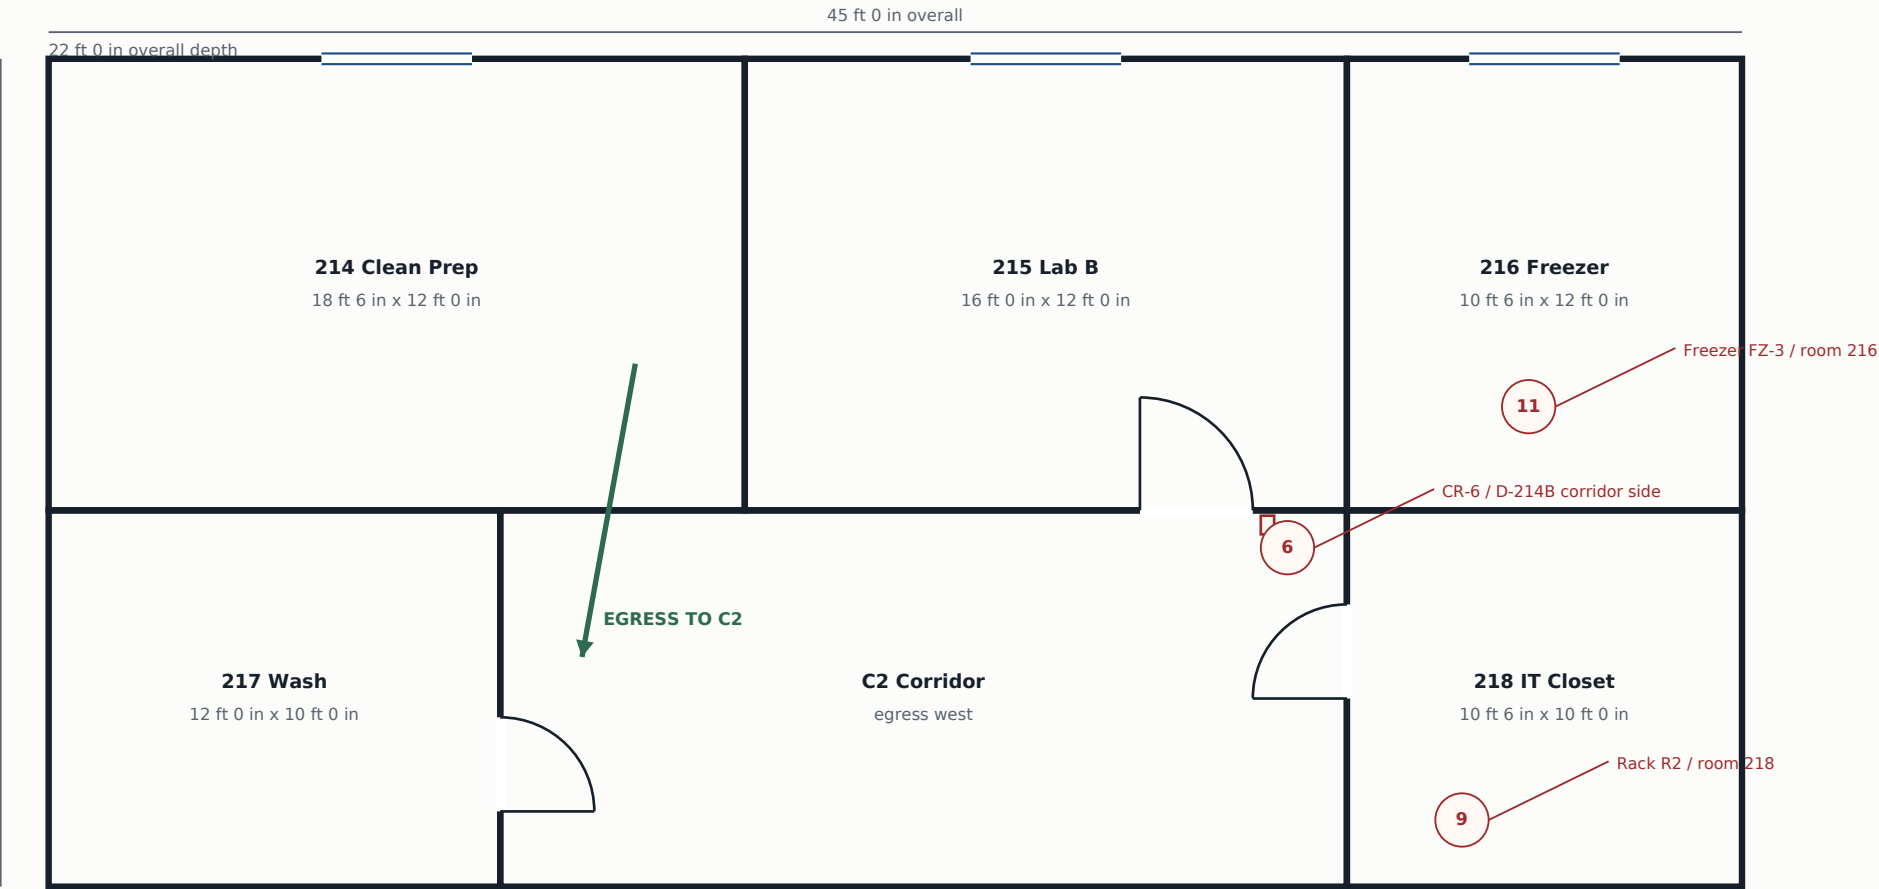

Location	Field condition	Coordinated artifact
214 Clean Prep	D214-01 tablet dock	CS-2/01; VLAN 210
215 Lab B	D-214B; CR-6 corridor side	CS-2/07; L2-15
216 Freezer	FZ-3 at callout 11	CS-2/12; VLAN 240; L2-17
218 IT Closet	Rack R2 at callout 9	CS-2/19; L2-19


T4.08 - Rack R2 elevation

IT Closet 218 | front elevation and patch schedule

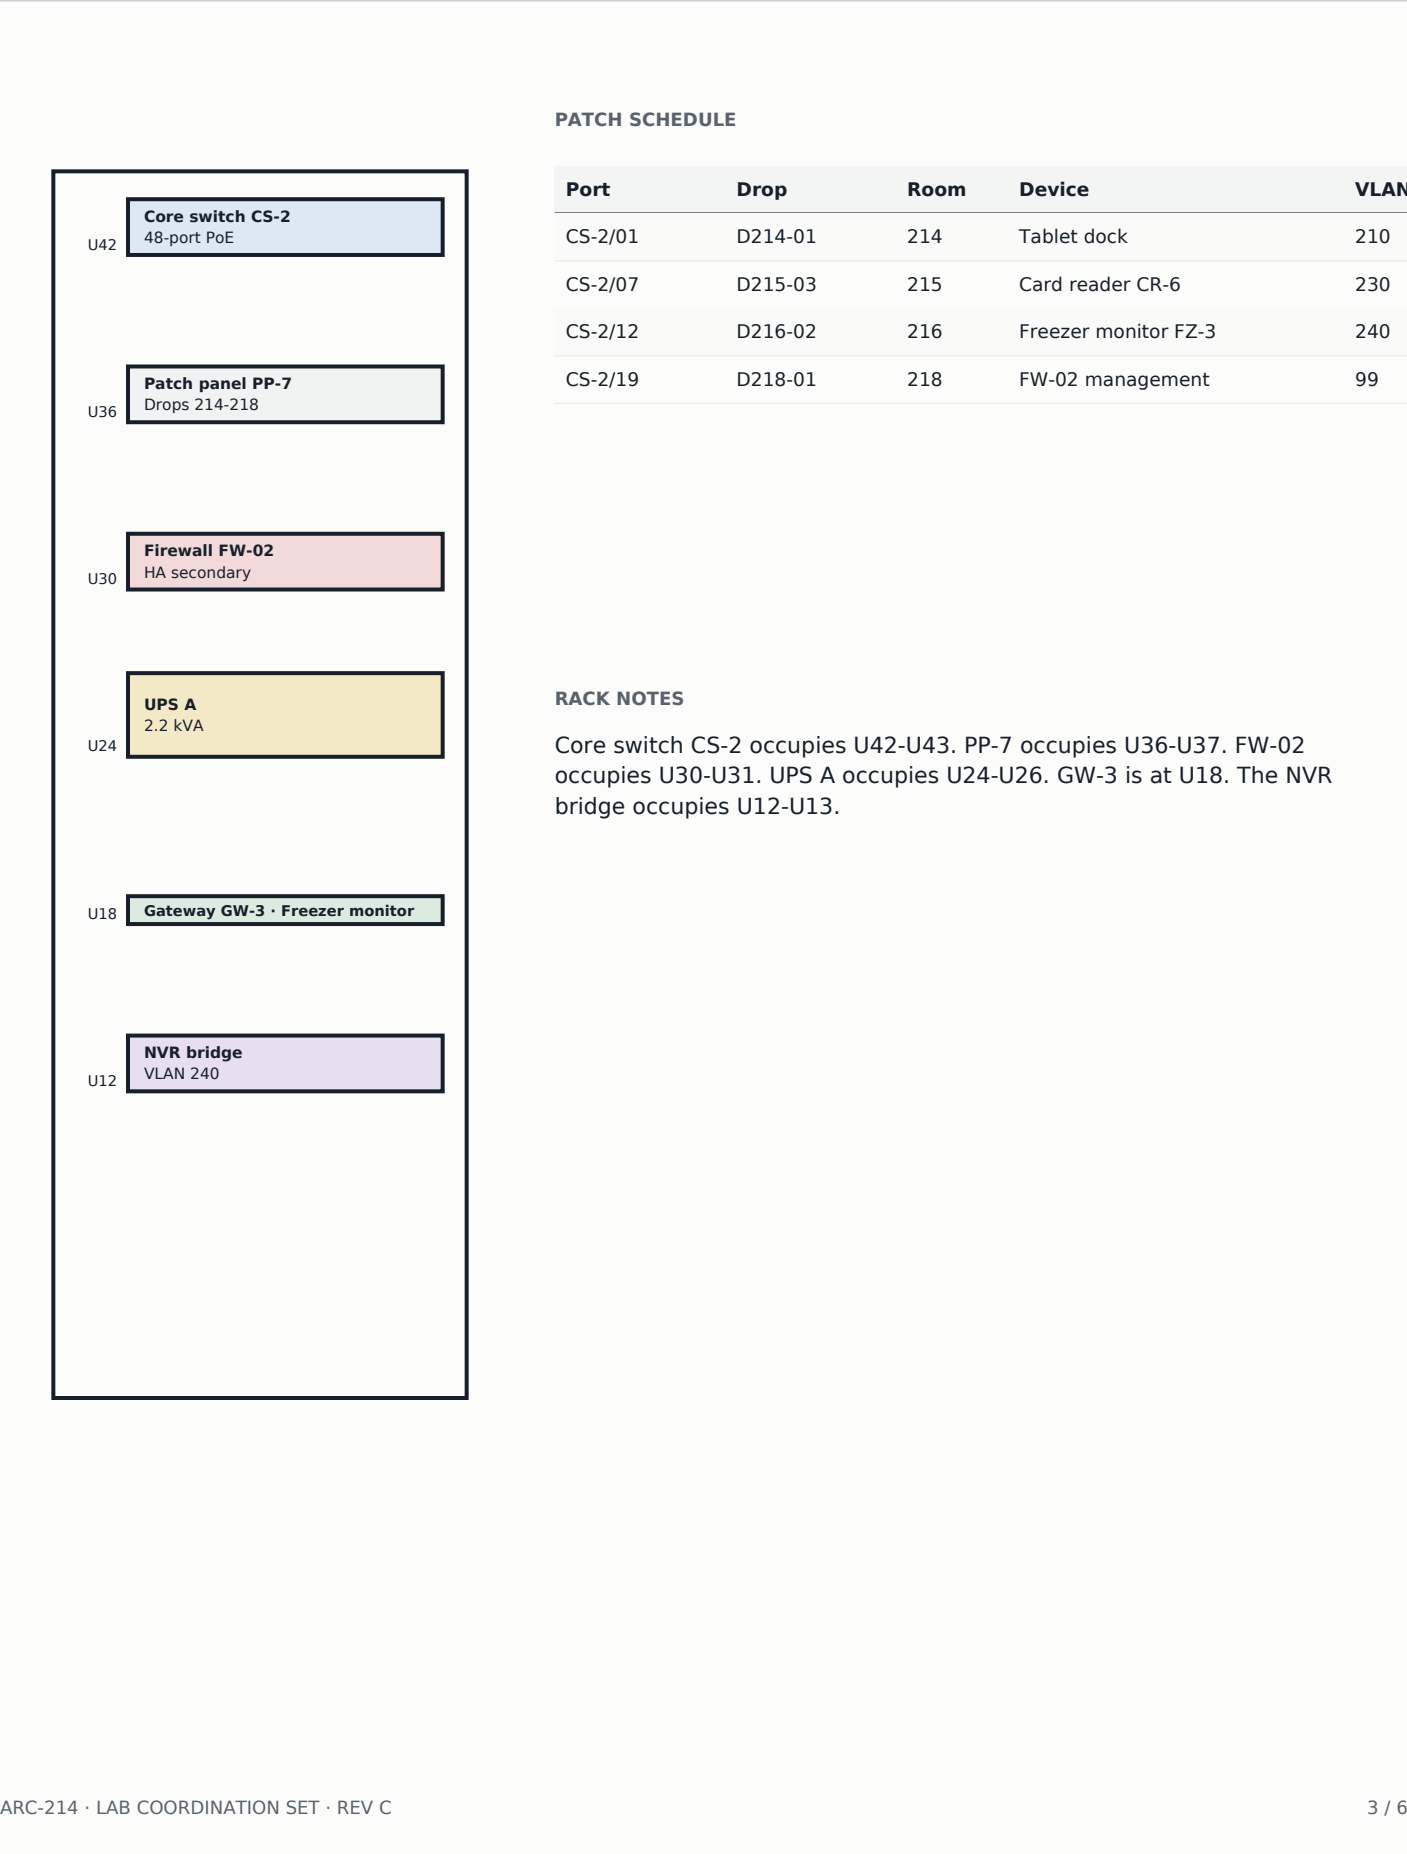

N1.07 - Laboratory network topology

Directed service paths and access-control policy

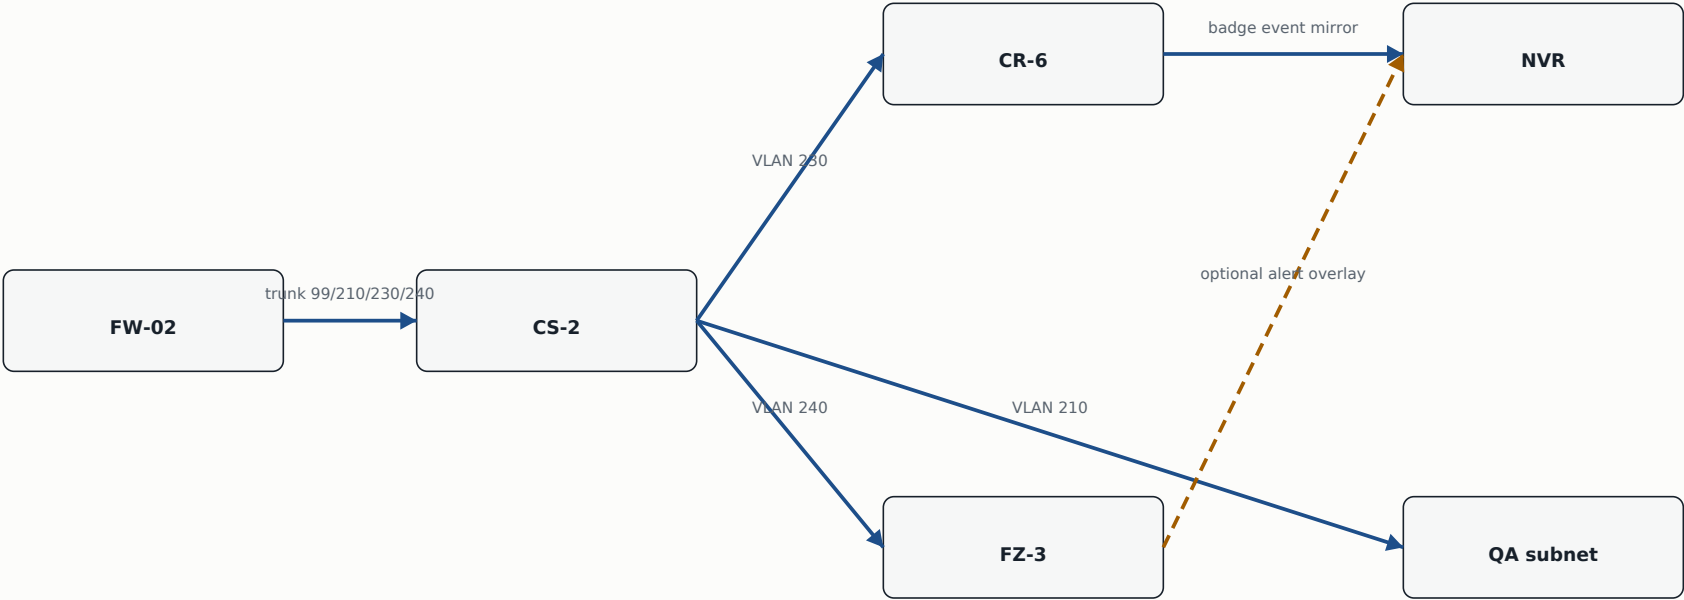

Rule	Source	Destination	VLAN	State
ACL-230-06	CR-6	NVR event mirror	230 -> 240	Permit one-way
SVC-210-QA	CS-2	QA subnet	210	Permit telemetry
TRK-FW02-CS2	FW-02	CS-2	99/210/230/240	Tagged trunk
OPT-CAM	FZ-3	NVR	240	Optional / dashed

E6.02 - Panel LP-2 schedule

Connected loads and emergency-branch coordination

Circuit	Load	Breaker	Emergency	Room	Note
L2-11	Bench outlets B	20A/1P	No	215	GFCI
L2-13	Autoclave AC-1	30A/2P	No	217	Dedicated
L2-15	Door controller DC-6	20A/1P	Yes	215	Feeds CR-6
L2-17	Freezer FZ-3	20A/1P	Yes	216	Monitor required
L2-19	Rack R2 UPS	20A/1P	Yes	218	UPS A
L2-21	Spare	20A/1P	No	-	Hold for Rev D

LOAD SUMMARY

Branch	Connected	Emergency	Coordination note
Normal receptacles	3.2 kVA	0.0 kVA	Bench and autoclave
Access control	0.4 kVA	0.4 kVA	DC-6 on L2-15
Cold storage	0.7 kVA	0.7 kVA	FZ-3 on L2-17
IT / UPS	1.1 kVA	1.1 kVA	R2 UPS on L2-19
Spare capacity	2.6 kVA	-	L2-21 held for Rev D

ISSUE CHECKS

- ☒ Emergency labels match floor-plan callouts
- ☐ L2-21 released for construction
- ☐ Freezer monitor moved to normal power

RFI-214B - Lab B corridor door

Scanned field response attached to Revision C issue record

ORION BIOLOGICS / FIELD RFI RESPONSE

RFI 214B ACCESS CONTROL / ARCHITECTURAL

Opened: 09 Jun 2026 Required on site: 13 Jun 2026

QUESTION

CAD Revision B identifies the Lab B corridor door as D-214A.

Field sticker and security rough-in identify D-214B.

Confirm door, reader side, and electrical circuit.

ARCHITECT RESPONSE

Use D-214A for the Lab B corridor door.

Corrected: use D-214B. Add reader CR-6 on corridor side.

Assign panel LP-2 circuit L2-15. Update access-control schedule.

Revision C dated 12 Jun 2026 governs.

D-214B

A. Verma, Architect of Record signed 12 Jun 2026

Security review TN contractor ack 13 Jun 2026

✓

Field	Revision B	Revision C
Door identifier	D-214A	D-214B
Reader	None	CR-6 corridor side
Circuit	Unassigned	L2-15
Schedule	Draft	Issued
