

Northwest Pilot Readiness Review

Meridian Retail Network | Steering packet | 10 August 2026

CONDITIONAL GO

DECISION REQUESTED

Authorize the six-store pilot for the 14 August 2026 launch window, subject to closure of the Bend gateway exception and recovery of Tier 2 service-desk backlog to the approved limit.

OPERATING CONTEXT

The launch covers six stores, two fulfillment nodes, and three payment partners. Friday's activation target is 4,850 devices. Spokane North completed training after the scheduled cutover rehearsal; Bend still has one open POS-to-gateway exception.

Finance approved reserve use for gateway freight and temporary floor support only. The Portland service desk remains above its Tier 2 launch threshold after the weekend migration. Signage reprint is deferred and is not reserve eligible.

DECISION REGISTER

Item	Owner	Due	State	Condition
Gateway freight reserve	Iris Wu	11 Aug	Approved	\$18.4k cap
Bend POS exception	Mateo Ruiz	12 Aug 17:00	Open	close before go
Service desk staffing	Priya Nair	13 Aug 09:00	Conditional	Tier 2 <= 22
Signage reprint	Noah Klein	Deferred	Not funded	outside reserve


HOLD CONDITIONS

Hold if Bend remains open after 12 Aug 17:00, payment-switch errors exceed 1.2%, or Tier 2 backlog exceeds 22 at launch review.


Launch metrics

Cutover snapshot | data through Friday 16:00 PT

DEVICE ACTIVATIONS

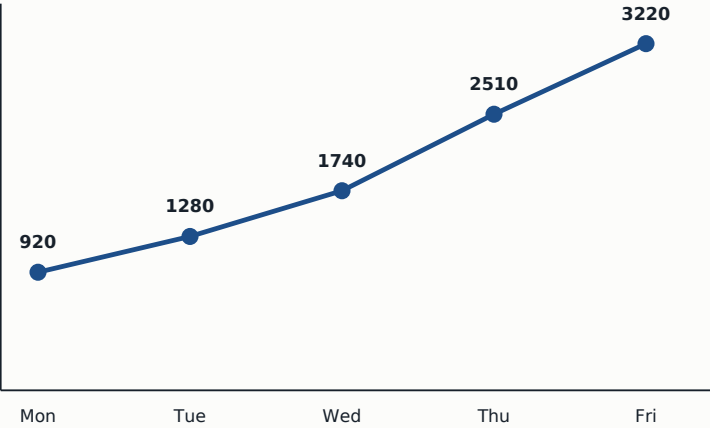

OPEN / BLOCKED BACKLOG

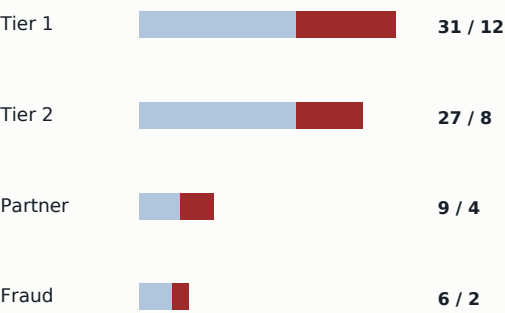

LAUNCH GUARDRAILS

Guardrail	Current	Limit	State
Payment-switch errors	0.9%	<= 1.2%	Inside
Tier 2 backlog	27	<= 22	Outside
Gateway spare units	126	>= 140	Outside
Training completion	92%	>= 95%	Outside

TRAFFIC-LIGHT CONVENTION

INSIDE


WATCH

OUTSIDE

Inside = limit met; Watch = caution; Outside = limit missed.
Blocked counts are a subset of open backlog, not an additional queue total.

Payment and device dependencies

Launch path and monitored fallback

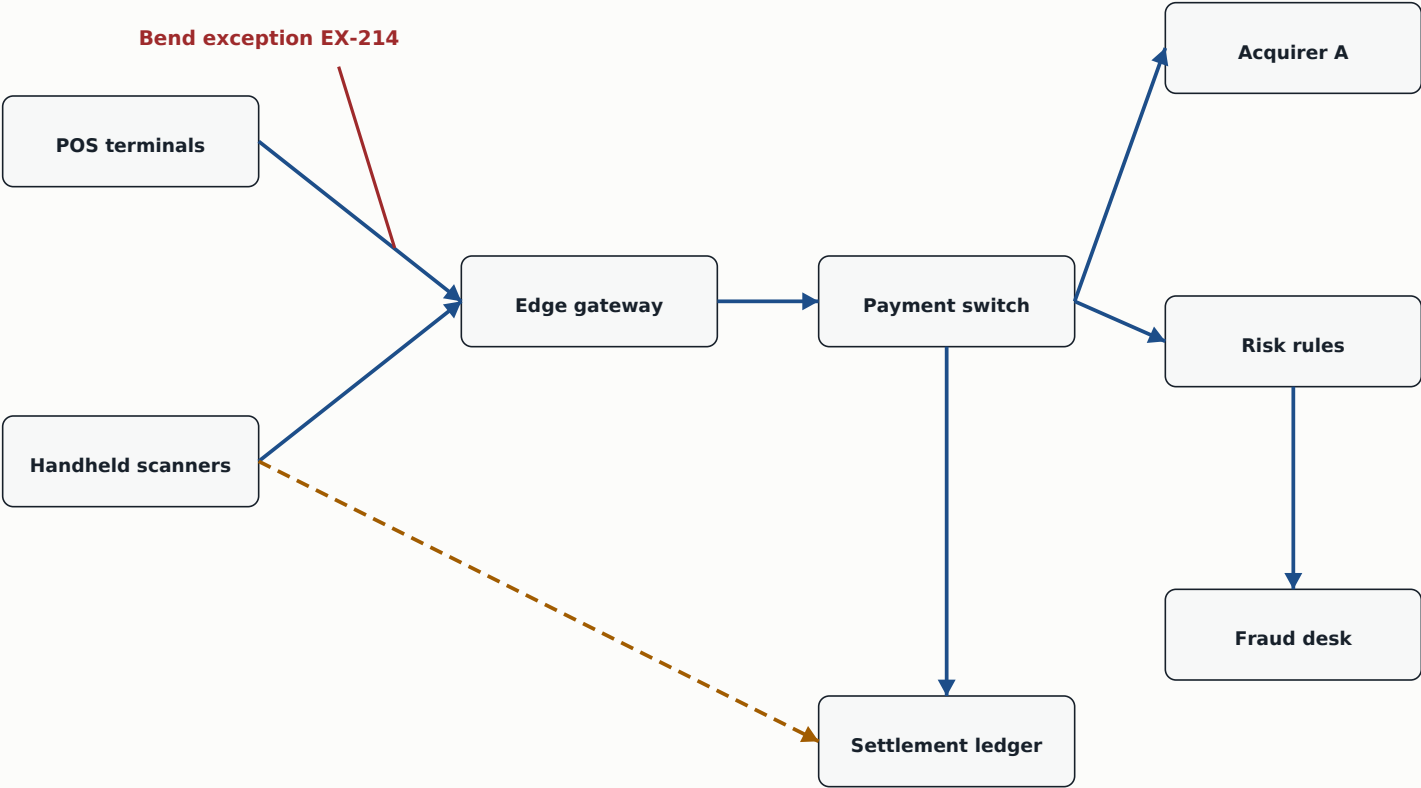

PATH NOTES

Mark	Meaning	State
Solid	Authorization or control path	Required
Dashed	Scanner event copy to settlement	Monitoring only
EX-214	Bend POS-to-gateway handshake	Open

Store readiness

Owner review at 10 August 15:30 PT

Store	Owner	Training	Gateways	Signage	POS	Staffing	Open item
PDX-02 Pearl	Lena	OK	144	OK	OK	OK	partner token
PDX-05 East	Owen	Watch	148	OK	OK	OK	coach shift
SEA-04 Ballard	Nia	OK	151	OK	OK	Watch	late coverage
SPK-03 North	Eli	Watch	146	OK	OK	OK	retest logged
BND-01 Bend	Mateo	OK	126	OK	Blocked	OK	EX-214 gateway
EUG-02 River	Sara	OK	143	Watch	OK	OK	signage ETA

OWNER NOTES

- 01 PDX-05 coach shift is scheduled before the Thursday close rehearsal.
- 02 SPK-03 training retest is logged; the dashboard still shows the packet-time Watch state.
- 03 BND-01 replacement gateway is staged at the Redmond depot; courier release remains pending EX-214 closure.
- 04 EUG-02 signage ETA does not use gateway reserve funds.

NEXT REVIEW AND PACKET CUT

Owners reconvene 13 August at 09:00 PT. Store states are frozen to the 10 August 15:30 PT packet cut; later field updates require an annotated change record.

Escalation matrix

Functional owner status by store

FUNCTIONAL ESCALATION MATRIX				
	Gateway	POS	Staffing	Partner
PDX-02	G	G	G	Y ●
PDX-05	Y /	G	G	G
SEA-04	G	G	Y	G
SPK-03	G	Y	G	G
BND-01	R	R /	Y	R / ●
EUG-02	G	G	G	Y

G clear Y watch R blocked / executive escalation dot external partner

ESCALATION CONVENTION

A slash marks required executive escalation. A dot marks external-partner action. Symbols may appear together in one cell.

Launch reserve ledger

Approved categories and current exposure

Vendor	Purpose	Invoice	Eligibility	Paid	Exposure
LumenWorks	gateway freight	\$12,640	Eligible	\$0	\$12,640
FieldBridge	floor support	\$5,760	Eligible	\$2,000	\$3,760
SignPro	signage reprint	\$3,480	Not eligible	\$0	\$0
SwitchOps	monitoring cover	\$2,900	Not eligible	\$0	\$0
Northstar Print	counter cards	\$740	Not eligible	\$740	\$0

FINANCE NOTE

Partial payment applies only to FieldBridge. Non-eligible invoices remain in the packet but do not consume launch reserve.

RECONCILIATION

Line	Amount
Eligible invoices before payments	\$18,400
FieldBridge payment applied	-\$2,000
Remaining eligible exposure	\$16,400

APPROVAL TRAIL

Finance controller Iris Wu approved the \$18,400 eligible invoice base on 9 August. The \$2,000 FieldBridge payment posted on 10 August at 12:40 PT; the reconciliation above is after that posting.

Appendix C - 7 August working snapshot

Version 0.7 | Superseded by steering packet issued 10 August 2026

Field	Working value	Status on 7 Aug
Steering decision	GO	draft
Tier 2 backlog	18	draft
Gateway spare units	158	draft
Bend POS	OK	draft
Reserve exposure	\$17,300	draft

Supersession record

Version 0.7 was replaced in full by OPS-NW-26-08 on 10 August at 09:15 PT. No value on this page is current.
