

Northwest Pilot Launch Dossier

Prepared for: Retail Operations Steering Committee | Packet date: 2026-08-10 | Status: conditional go

Executive memo

The Northwest pilot can proceed only if store enablement, gateway inventory, and payment-switch monitoring stay inside the launch guardrails. The program remains a conditional go because Spokane North cleared training late, Bend has one unresolved POS gateway exception, and the Portland service desk still has elevated Tier 2 backlog after the weekend migration. The visible decision log below supersedes the draft appendix included at the end of this packet.

Launch scope covers six stores, two fulfillment nodes, and three payment partners. The activation target is 4,850 devices by Friday close. Finance approved the reserve draw only for gateway freight and temporary floor support; signage reprint remains unfunded. Operations must preserve the Monday risk snapshot, chart values, and dependency diagram because several values are not repeated in body text.

Visible steering decision: CONDITIONAL GO. Hold criteria: Bend POS exception open after 2026-08-12 17:00, payment-switch error rate above 1.2%, or Tier 2 backlog above 22 at launch review.


Decision item	Owner	Due	State	Condition
Gateway freight reserve	Iris	2026-08-11	Approved	\$18.4k cap
Bend POS exception	Mateo	2026-08-12 17:00	Open	must close before go
Service desk staffing	Priya	2026-08-13 09:00	Conditional	Tier 2 backlog <= 22
Signage reprint	Noah	deferred	Not funded	do not include in reserve

Packet order: memo, dashboard, dependency map, store readiness, escalation heatmap, procurement, draft appendix.


Launch Metrics Dashboard

All panels are visible dashboard exports. Values in charts are part of the launch record.

Device activations by day

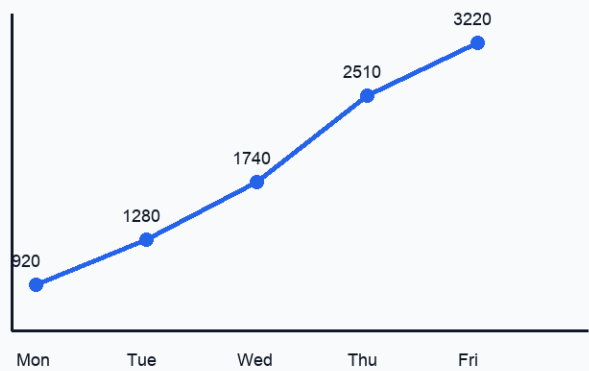

Backlog by queue

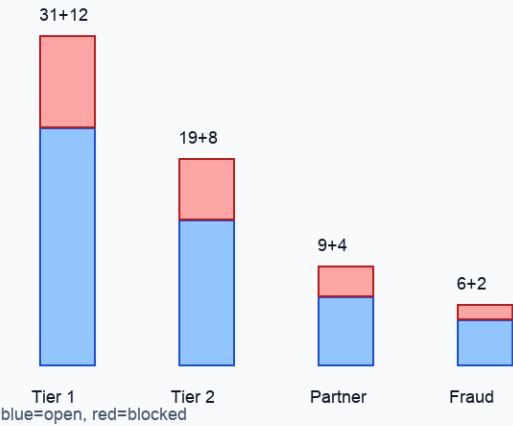


Guardrail	Limit	Current	State
Payment-switch error rate	<=1.2%	0.9%	OK
Tier 2 backlog	<=22	27	At risk
Gateway inventory buffer	>=140	126	Breach
Store training completion	>=95%	92%	At risk

Dashboard warning: review the guardrail table before launch review. Conditional go does not become final until the Bend exception is closed and service-desk load is back inside threshold.

Dependency Map - Payment Activation Path

Solid arrows are required launch dependencies. Dashed arrows are fallback paths.

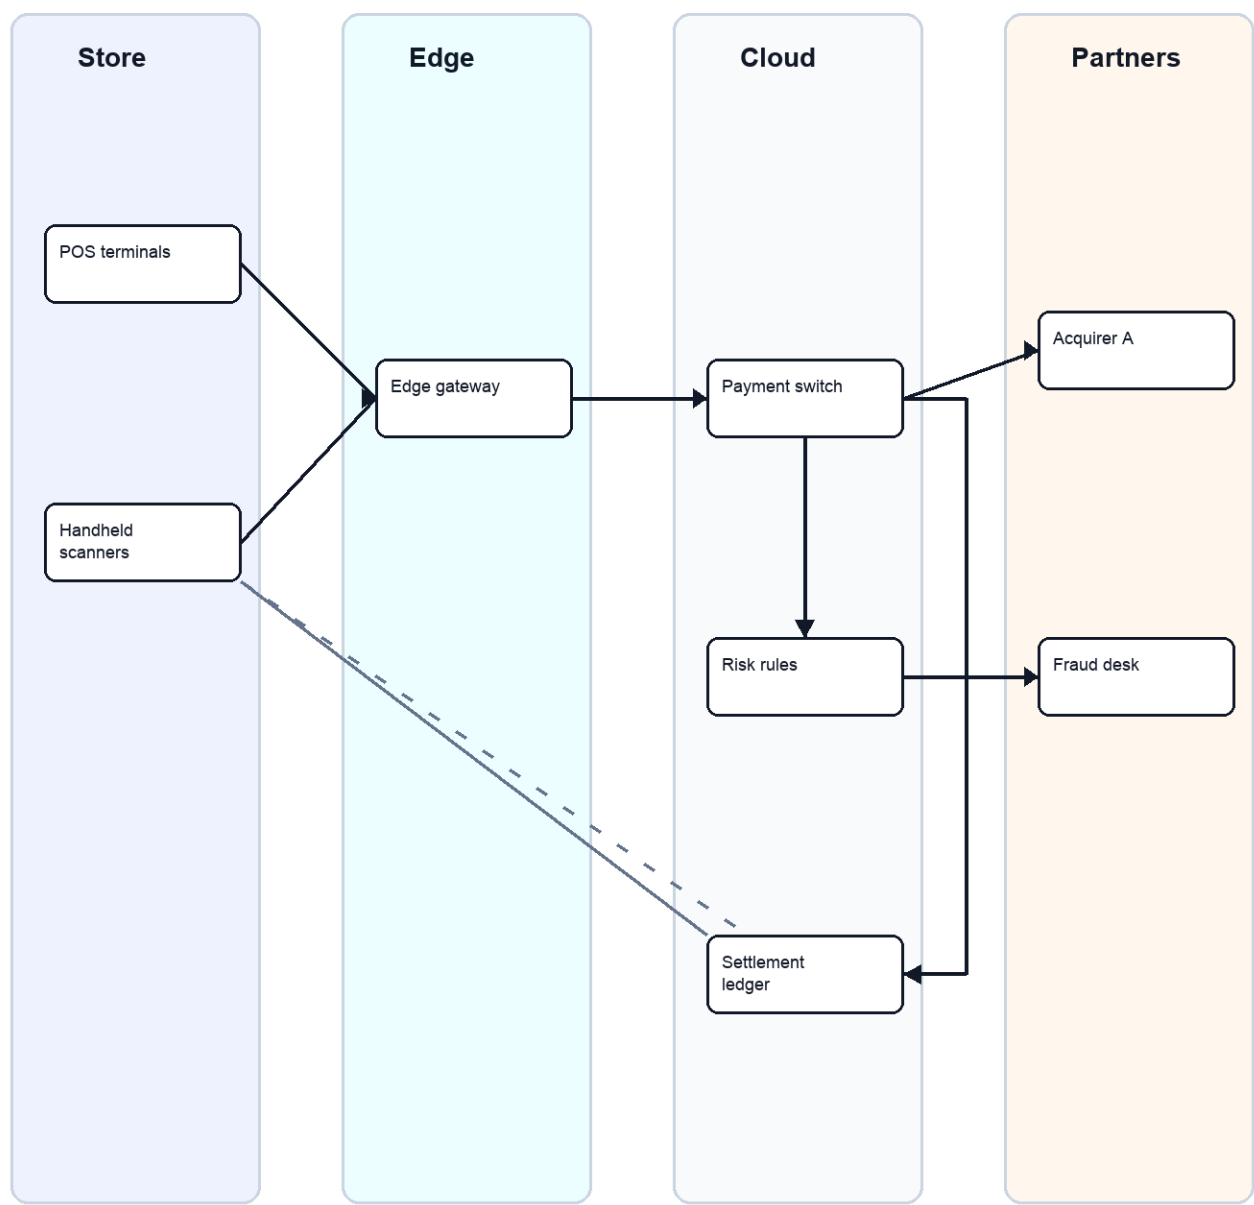

Map note: Bend POS exception is on the POS terminals to Edge gateway dependency. Fallback handheld-to-ledger path exists but does not satisfy payment authorization.

Store Readiness Register

Status register exported from the launch tracker. Abbreviations: OK, AR=at risk, BLK=blocked.

Store	Mgr	Training	Gateways	Signage	POS	Staffing	Open issue
SEA-01 Pike	Mina	OK	148	OK	OK	OK	none
SEA-04 Ballard	Ravi	OK	136	OK	OK	AR	temp floor support
PDX-02 Pearl	Jon	OK	142	OK	OK	OK	none
PDX-05 East	Lena	AR	131	OK	OK	OK	training makeup Thu
BND-01 Bend	Mateo	OK	126	OK	BLK	OK	gateway exception
SPK-03 North	Asha	AR	144	OK	OK	AR	late completion

Exception: BND-01 Bend is the only blocked POS row. It also has the lowest gateway count at 126.

Training risk: PDX-05 East and SPK-03 North are at risk. SEA-04 Ballard staffing is at risk but training is OK.

Escalation Matrix - Store x Workstream

Launch operations matrix - status letter, escalation slash, and partner dot are all part of the cell state.

	Training	Gateway	POS	Staffing	Partner
SEA-01	G clear	G clear	G clear	G clear	G clear
SEA-04	G clear	Y watch	G clear	Y watch	G clear
PDX-02	G clear	G clear	G clear	G clear	Y watch ●
PDX-05	Y watch	Y watch /	G clear	G clear	G clear
BND-01	G clear	R blocked	R blocked /	Y watch	R blocked / ●
SPK-03	Y watch	G clear	G clear	Y watch	G clear

LEGEND AND EXCEPTION NOTES

G = clear, Y = watch, R = blocked. A red slash means executive escalation. A black dot means external partner follow-up is required.

Readout: BND-01 has blocked Gateway, POS, and Partner cells. PDX-05 has a Gateway slash but POS is clear. PDX-02 Partner has a dot without a red block.

Procurement and Reserve Ledger

Line	Vendor	Purpose	Amount	Reserve eligible	Paid
1	LumenWorks	gateway freight expedite	\$12,640	Yes	No
2	FieldBridge	temporary floor support	\$5,760	Yes	Partial \$2,000
3	SignPro	signage reprint	\$3,480	No	No
4	SwitchOps	payment monitor extension	\$2,900	Yes	No
5	Northstar Print	training packet reprint	\$740	No	Paid

Reserve subtotal before payment: \$21,300.
FieldBridge partial payment: -\$2,000.
Remaining eligible reserve exposure:
\$19,300.

Accounts payable note: PARTIAL
PAID applies only to
FieldBridge, not to the whole
ledger. Signage reprint is not
reserve eligible.

PARTIAL PAID

Draft Appendix - Superseded Values

DRAFT APPENDIX - retained for audit context only

Draft field	Draft value	Visible final value	Disposition
Launch decision	GO	CONDITIONAL GO	superseded
Tier 2 backlog	18	27	superseded
Gateway inventory buffer	158	126	superseded
Bend POS	OK	BLK/open exception	superseded
Reserve exposure	\$17,300	\$19,300	superseded

Audit note: do not replace final dashboard or ledger values with this draft appendix. It exists to show why the steering decision changed after Monday risk review.
